


ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Qtr 2, 2026 Apr	May	Jun
0			The Cage Data Analytics Implementation	172 days	Mon 4/05/26	Tue 29/12/26					
1			Phase 1: Project Initiation & Data Discovery	30 days	Mon 4/05/26	Fri 12/06/26					
2			Conduct stakeholder alignment workshop with Sanjay Danani and Anthony P.V.	3 days	Mon 4/05/26	Wed 6/05/26		Sanjay Danani,Anthony P.V.,Project Manager			
3			Define project charter objectives and boundaries	4 days	Thu 7/05/26	Tue 12/05/26	2	Data Analyst,Project Manager			
4			Draft high-level business requirements document (BRD)	4 days	Wed 13/05/26	Mon 18/05/26	3	Data Analyst			

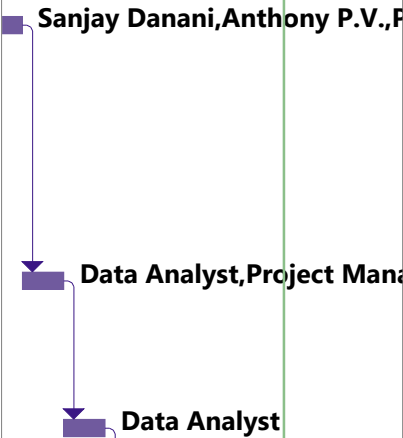

Project: The Cage Data Analytic Date: Sun 14/06/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

ID	 Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Qtr 2, 2026 AprMayJun		
5		Formulate comprehensive data governance framework	4 days	Tue 19/05/26	Fri 22/05/26	4	Data Analyst			 Data Analyst
6		Establish corporate data security and access protocols	2 days	Mon 25/05/26	Tue 26/05/26	5	Data Engineer			 Data Engineer
7		Evaluate ethical implications of tracking player performance data	2 days	Wed 27/05/26	Thu 28/05/26	6	Data Analyst, Sanjay Danani, Project Manager			 Data Analyst, Sanjay Danani, Project Manager
8		Define data privacy boundaries and player consent mechanisms	2 days	Fri 29/05/26	Mon 1/06/26	7	Data Analyst			 Data Analyst
9		Establish data quality and validation standards	2 days	Tue 2/06/26	Wed 3/06/26	8	Data Analyst, Data Engineer			 Data Analyst, Data Engineer

Project: The Cage Data Analytic

Date: Sun 14/06/26

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone















Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only















External Tasks

External Milestone

Deadline

Progress

Manual Progress











ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Qtr 2, 2026 AprMayJun		
10			Review data compliance against regional privacy laws	2 days	Thu 4/06/26	Fri 5/06/26	9	Data Analyst			 Data Analyst
11			Present project charter to executive steering committee	2 days	Mon 8/06/26	Tue 9/06/26	10	Data Analyst, Sanjay Danani, Anthony P.V., Project Manager			 Data Analyst
12			Secure formal sign-off for the project charter	3 days	Wed 10/06/26	Fri 12/06/26	11	Sanjay Danani, Anthony P.V., Project			 Sanjay D
13			M1: Project Charter & Governance Framework Approved	0 days	Fri 12/06/26	Fri 12/06/26	12				 12/06
14			Phase 2: Requirements & Technical Gap Analysis	27 days	Mon 15/06/26	Tue 21/07/26					

Project: The Cage Data Analytic

Date: Sun 14/06/26

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone















Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only















External Tasks

External Milestone

Deadline

Progress

Manual Progress












ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Qtr 2, 2026		
									Apr	May	Jun
15			Analyze Dictionaries and Configure Automated Odoo ERP Delta Loading	3 days	Mon 15/06/26	Wed 17/06/26	13	Data Engineer			 Data E
16			Perform operational field studies in Singapore	3 days	Thu 18/06/26	Mon 22/06/26	15	Data Analyst			 Dat
17			Consolidate field study findings into a baseline report	3 days	Tue 23/06/26	Thu 25/06/26	16	Data Analyst			 D
18			Identify gaps in current automated data capture systems	3 days	Fri 26/06/26	Tue 30/06/26	17	Data Analyst,Data Engineer			



Project: The Cage Data Analytic

Date: Sun 14/06/26

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone















Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only















External Tasks

External Milestone

Deadline

Progress

Manual Progress











ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Qtr 2, 2026			
					Apr					May		Jun
19			Identify technical data gaps (specifically the workflow to capture the other 9 players).	4 days	Wed 1/07/26	Mon 6/07/26	18	Data Analyst,Data Engineer				
20			Document technical source-to-target data mappings	4 days	Tue 7/07/26	Fri 10/07/26	19	Data Engineer				
21			Conduct data data gap review workshop with engineering team	3 days	Mon 13/07/26	Wed 15/07/26	20	Data Analyst,Data Engineer,Project Manager				
22			Finalize Technical Requirements Baseline Document	4 days	Thu 16/07/26	Tue 21/07/26	21	Data Analyst,Project Manager				

--

Project: The Cage Data Analytic Date: Sun 14/06/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

ID	 Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Qtr 2, 2026 Apr May Jun		
23		M2: Technical Data Audit Completed	0 days	Tue 21/07/26	Tue 21/07/26	22				
24		M3: Requirements Baseline Signed Off	0 days	Tue 21/07/26	Tue 21/07/26	23				
25		Phase 3: System Architecture & Infrastructure Procurement	37 days	Wed 22/07/26	Thu 10/09/26					
26		Host infrastructure planning workshops with VU Information Systems	3 days	Wed 22/07/26	Fri 24/07/26	24	Data Engineer, Project Manager			
27		Assess cloud computing and storage scalability requirements	3 days	Mon 27/07/26	Wed 29/07/26	26	Data Engineer			

Project: The Cage Data Analytic
Date: Sun 14/06/26

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone















Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only















External Tasks

External Milestone

Deadline

Progress

Manual Progress











ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Qtr 2, 2026		
									Apr	May	Jun
28			Evaluate network bandwidth constraints across regional branches	3 days	Thu 30/07/26	Mon 3/08/26	27	Data Engineer			
29			Design Target Cloud Architecture and OLAP Storage Models	4 days	Tue 4/08/26	Fri 7/08/26	28	Data Engineer			
30			Finalize hardware specification list for procurement	3 days	Mon 10/08/26	Wed 12/08/26	29	Data Engineer			
31			Submit formal procurement request to VU Information Systems Corp	2 days	Thu 13/08/26	Fri 14/08/26	30	Data Engineer			

--	--	--	--	--	--	--	--	--	--	--	--

Project: The Cage Data Analytic Date: Sun 14/06/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

ID	 Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Qtr 2, 2026 AprMayJun		
32		Negotiate service level agreements (SLAs) with cloud vendor	3 days	Mon 17/08/26	Wed 19/08/26	31	Data Engineer			
33		Process infrastructure procurement financial approvals (\$1.5M budget)	3 days	Thu 20/08/26	Mon 24/08/26	32	Sanjay Danani,Project Manager			
34		Provision primary cloud data warehouse environments	2 days	Tue 25/08/26	Wed 26/08/26	33	Data Engineer			
35		Configure development, testing, and production environments	2 days	Thu 27/08/26	Fri 28/08/26	34	Data Engineer			
36		Implement cloud firewall rules and IAM access roles	3 days	Mon 31/08/26	Wed 2/09/26	35	Data Engineer			

Project: The Cage Data Analytic Date: Sun 14/06/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Qtr 2, 2026			
					Apr					May		Jun
37			Conduct preliminary architectural security review	3 days	Thu 3/09/26	Mon 7/09/26	36	Data Engineer				
38			Sign off on infrastructure readiness	3 days	Tue 8/09/26	Thu 10/09/26	37	Data Analyst, Sanjay Danani, Project				
39			M4: System Architecture & Cloud Procurement Finalised. Infrastructure installation approved by VU	0 days	Thu 10/09/26	Thu 10/09/26	38	IT Systems Specialist				
40			Phase 4: Data Integration & Pipeline Engineering	37 days	Fri 11/09/26	Mon 2/11/26						
41			Configure staging environment	3 days	Fri 11/09/26	Tue 15/09/26	39	Data Engineer				

Project: The Cage Data Analytic
Date: Sun 14/06/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Qtr 2, 2026		
									Apr	May	Jun
42			Configure Odoo ERP Data Extraction and Automated ETL Delta Schedules	4 days	Wed 16/09/26	Mon 21/09/26	41	Data Engineer			
43			Establish data ingestion routines for regional operational inputs	4 days	Tue 22/09/26	Fri 25/09/26	42	Data Engineer			
44			Build custom API connectors for real-time player data feeds	3 days	Mon 28/09/26	Wed 30/09/26	43	Data Engineer			
45			Develop Data Cleaning and Structural Standardization Scripts	2 days	Thu 1/10/26	Fri 2/10/26	44	Data Engineer			

--

Project: The Cage Data Analytic Date: Sun 14/06/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Qtr 2, 2026		
									Apr	May	Jun
46			Build custom parsing logic for unstructured performance text fields	3 days	Mon 5/10/26	Wed 7/10/26	45	Data Engineer			
47			Create standard transformation tables within data warehouse	4 days	Thu 8/10/26	Tue 13/10/26	46	Data Engineer			
48			Implement error logging and automated notification mechanisms	3 days	Wed 14/10/26	Fri 16/10/26	47	Data Engineer			
49			Conduct Unit and Integration Testing of Data Pipeline Components	4 days	Mon 19/10/26	Thu 22/10/26	48	Data Engineer			

--

Project: The Cage Data Analytic Date: Sun 14/06/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Qtr 2, 2026		
									Apr	May	Jun
50			Optimize pipeline indexing for database query execution speeds	3 days	Fri 23/10/26	Tue 27/10/26	49	Data Engineer			
51			Conduct data volume stress tests on pipeline infrastructure	3 days	Wed 28/10/26	Fri 30/10/26	50	Data Engineer			
52			Execute final code freeze for integration layer	1 day	Mon 2/11/26	Mon 2/11/26	51	Data Engineer			
53			M5: Code Freeze & System Integration	0 days	Mon 2/11/26	Mon 2/11/26	52				
54			Phase 5: Analytics, Dashboarding & Deployment	41 days	Tue 3/11/26	Tue 29/12/26					

--

Project: The Cage Data Analytic Date: Sun 14/06/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

ID	 Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Qtr 2, 2026		
								Apr	May	Jun
55		Run master end-to-end data validation checks against source systems	3 days	Tue 3/11/26	Thu 5/11/26	53	Data Engineer			
56		Design Wireframes, Branding Standards, and Build Operational and Regional Dashboards	4 days	Fri 6/11/26	Wed 11/11/26	55	Data Analyst			
57		Extract aggregated datasets for advanced analytical analysis	3 days	Thu 12/11/26	Mon 16/11/26	56	Data Analyst			
58		Engineering historical data features for predictive modeling	3 days	Tue 17/11/26	Thu 19/11/26	57	ML engineer			

Project: The Cage Data Analytic
Date: Sun 14/06/26

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Progress

Manual Progress

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Qtr 2, 2026		
									Apr	May	Jun
59			Train machine learning models for predictive performance analysis	3 days	Fri 20/11/26	Tue 24/11/26	58	ML engineer			
60			Validate predictive model accuracy and adjust parameters	3 days	Wed 25/11/26	Fri 27/11/26	59	ML engineer			
61			Integrate predictive model outputs into final BI dashboards	2 days	Mon 30/11/26	Tue 1/12/26	60	Data Analyst,ML engineer			
62			Conduct user acceptance testing (UAT) with branch managers	3 days	Wed 2/12/26	Fri 4/12/26	61	Data Analyst,QA/Testir Leader.,Project Manager			

Project: The Cage Data Analytic Date: Sun 14/06/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Qtr 2, 2026			
					Apr					May		Jun
63			Remediate critical dashboard bugs identified during UAT cycles	3 days	Mon 7/12/26	Wed 9/12/26	62	Data Analyst				
64			Compile technical system documentation and user manuals	3 days	Thu 10/12/26	Mon 14/12/26	63	Data Analyst,Data Engineer				
65			Deliver operational training sessions to regional system users	2 days	Tue 15/12/26	Wed 16/12/26	64	Data Analyst,Change Management / Training Director,Project Manager				
66			Execute data synchronization for final production deployment	2 days	Thu 17/12/26	Fri 18/12/26	65	Data Engineer				

--

Project: The Cage Data Analytic Date: Sun 14/06/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

ID	 Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Qtr 2, 2026 Apr	May	Jun
67		Go-live: Deploy analytical dashboard platform to production	1 day	Mon 21/12/26	Mon 21/12/26	66	Data Engineer			
68		Monitor production stability and user access logs	3 days	Tue 22/12/26	Thu 24/12/26	67	Data Analyst			
69		Conduct post-deployment project review and compile lessons learned	2 days	Fri 25/12/26	Mon 28/12/26	68	Data Analyst, Data Engineer, ML engineer, Project Manager			
70		Archive project files and close out vendor accounts	1 day	Tue 29/12/26	Tue 29/12/26	69	Data Analyst, Project Manager			
71		M6: Project Closure	0 days	Tue 29/12/26	Tue 29/12/26	70				

Project: The Cage Data Analytic
Date: Sun 14/06/26


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

Project Manager


nager


Project: The Cage Data Analytic
Date: Sun 14/06/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

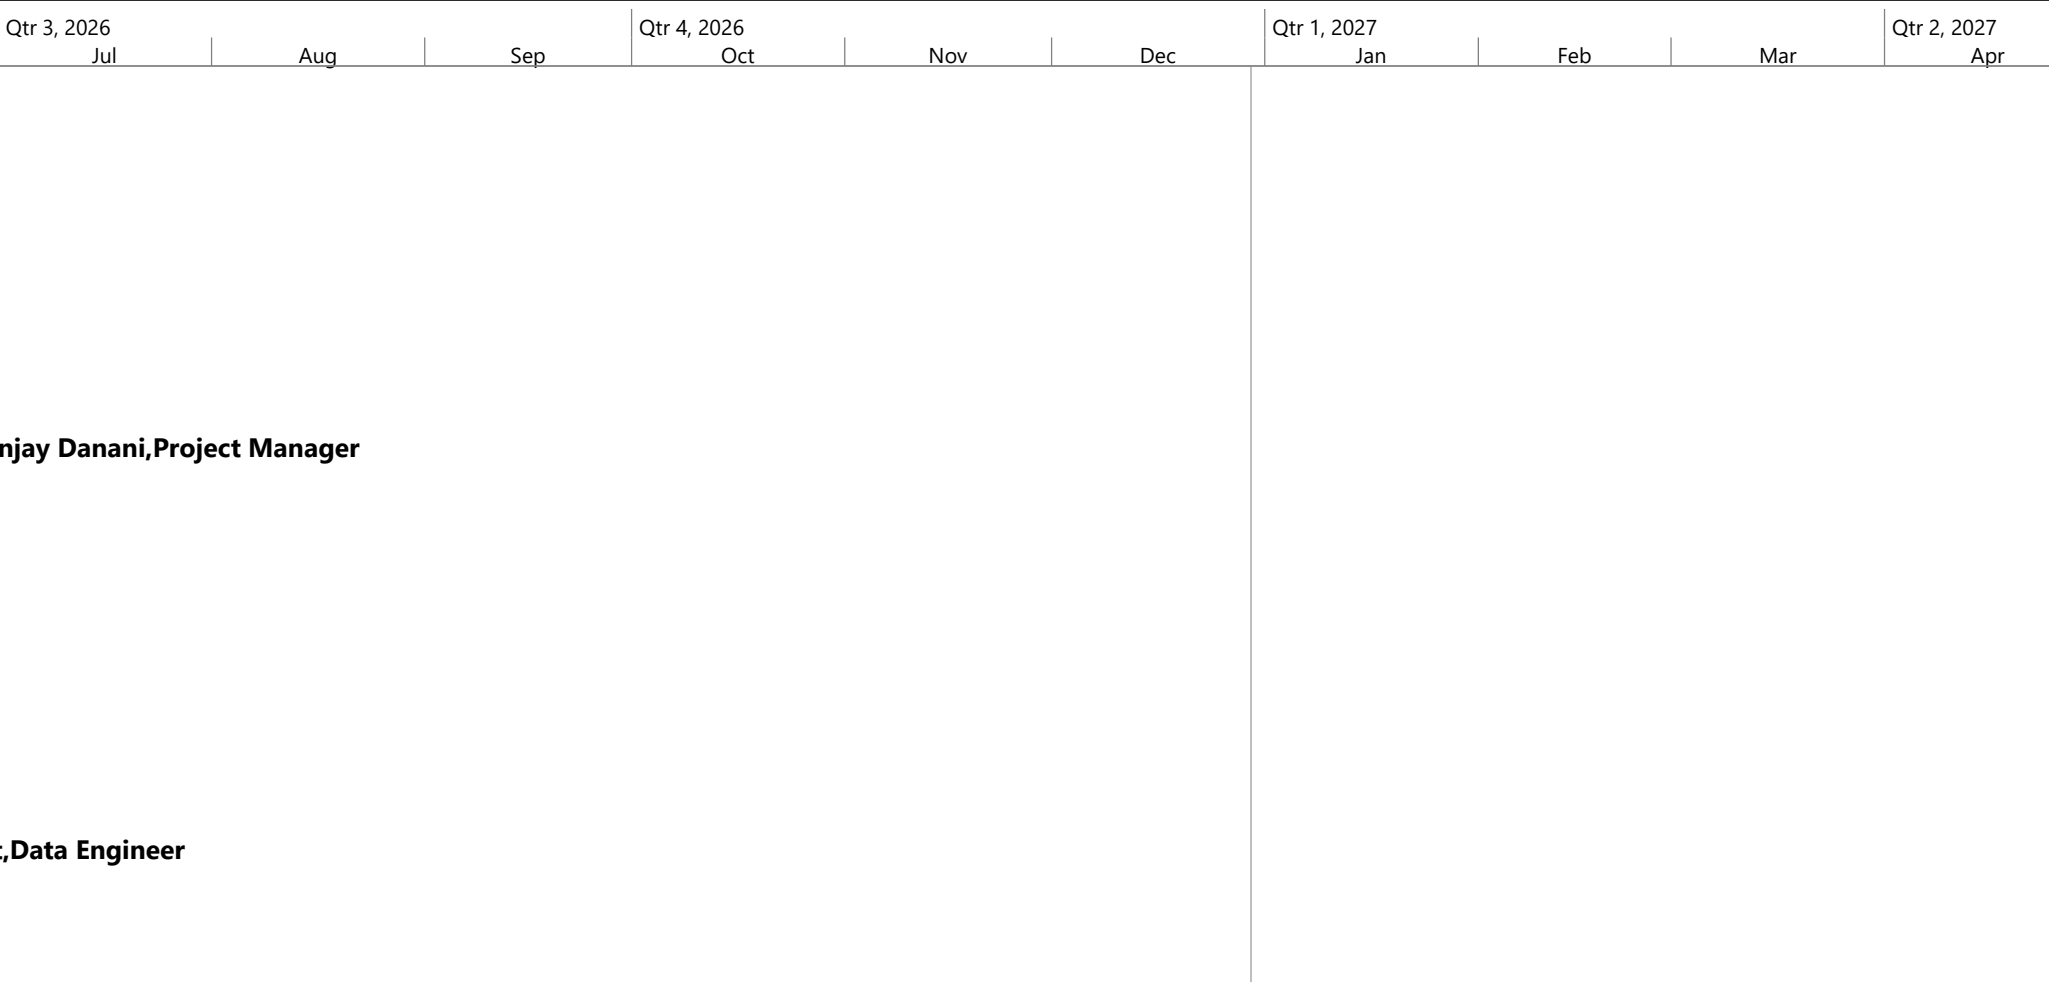


Project: The Cage Data Analytic Date: Sun 14/06/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

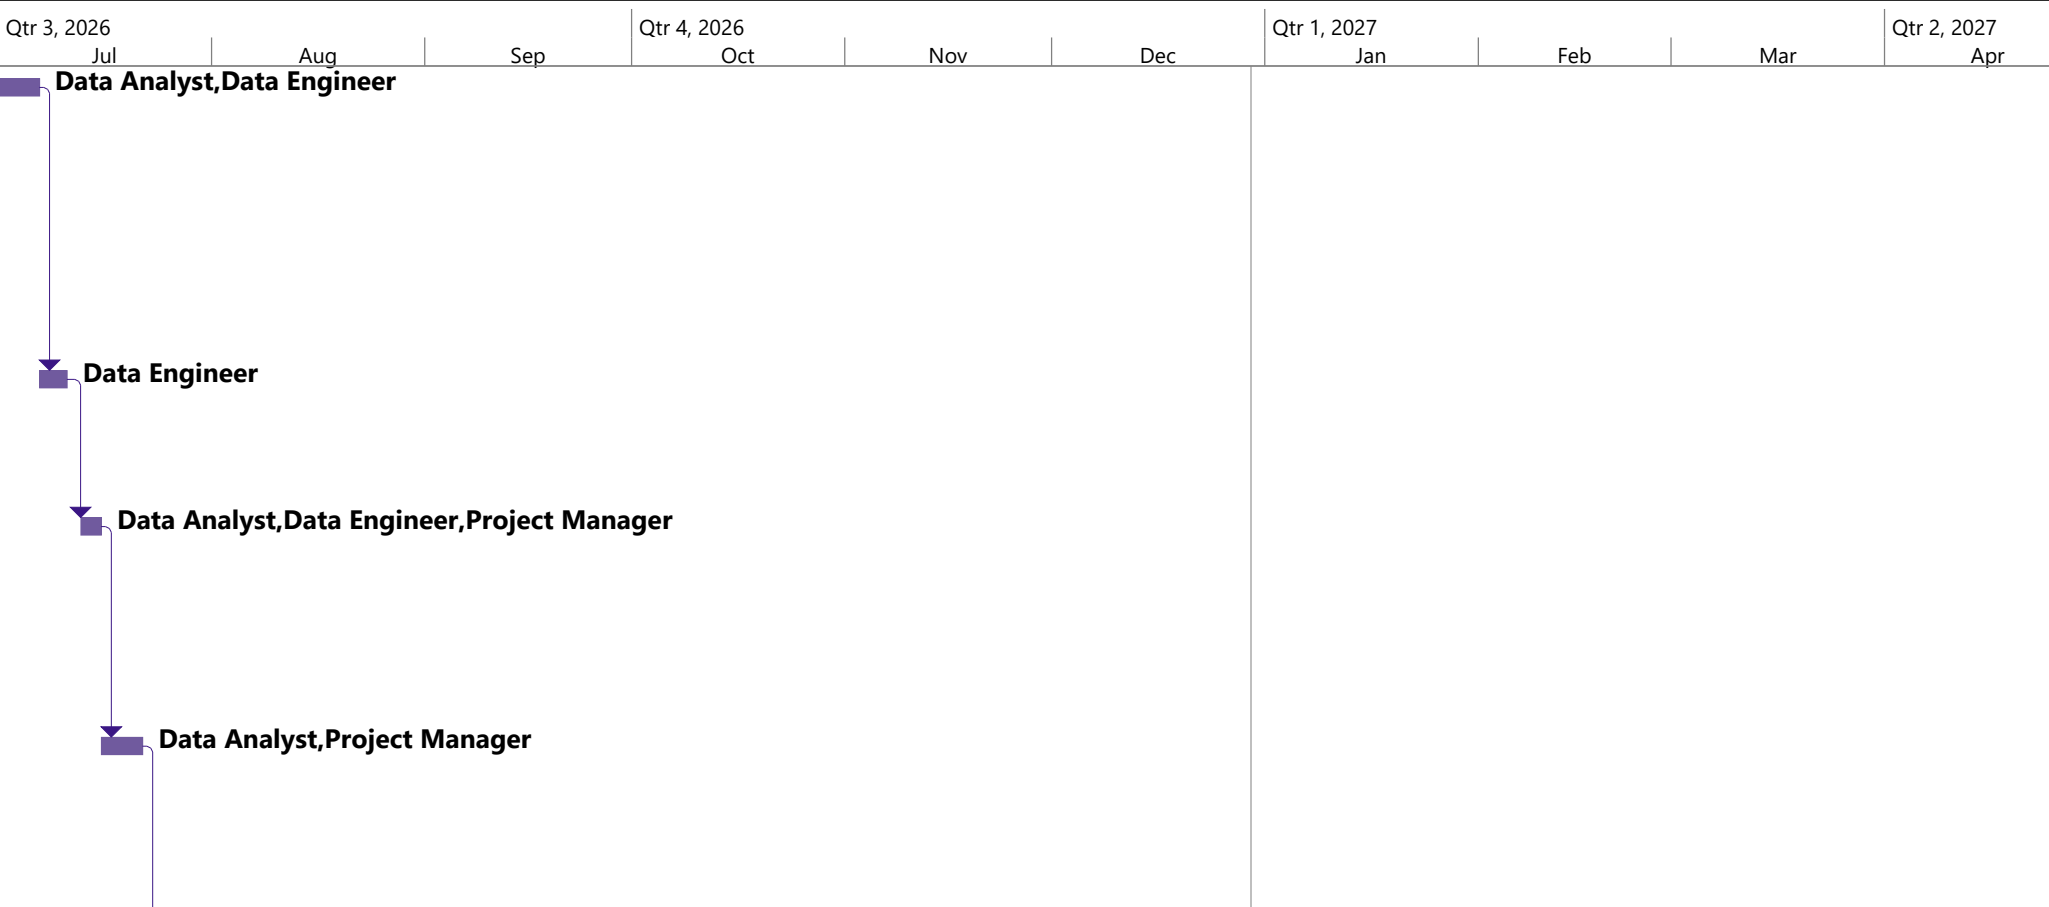


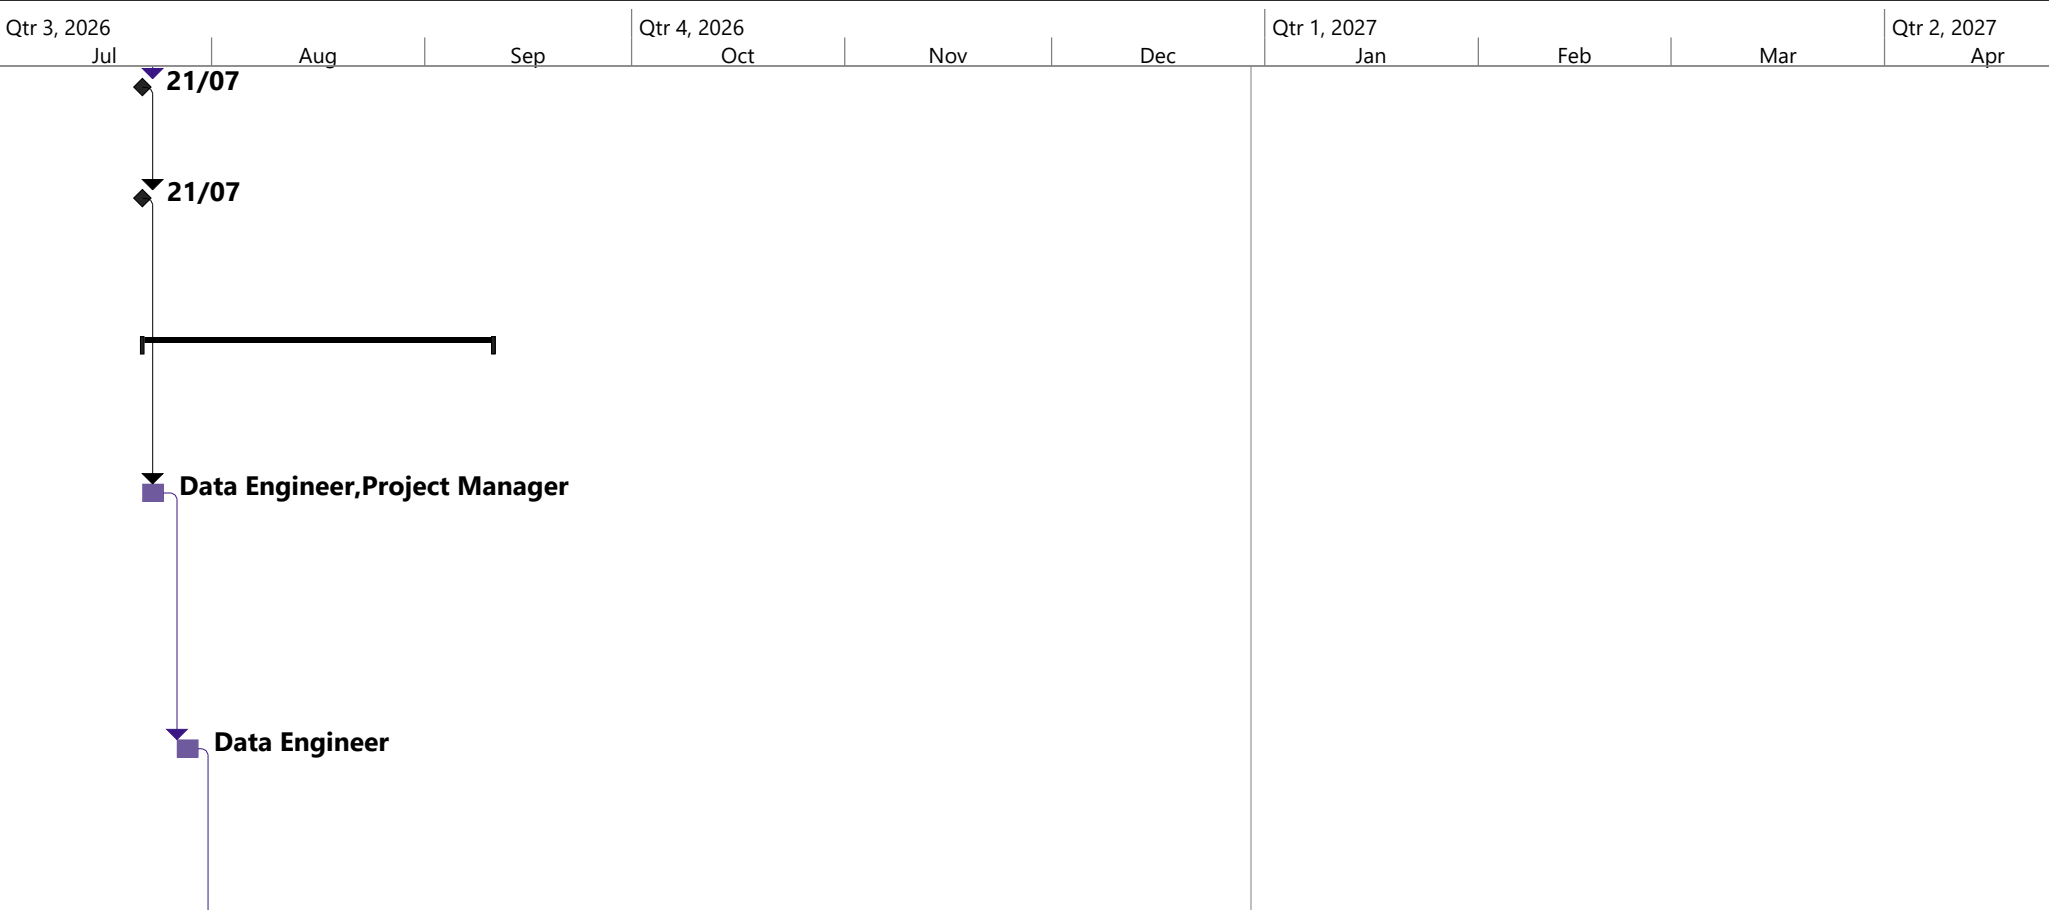


Project: The Cage Data Analytic Date: Sun 14/06/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

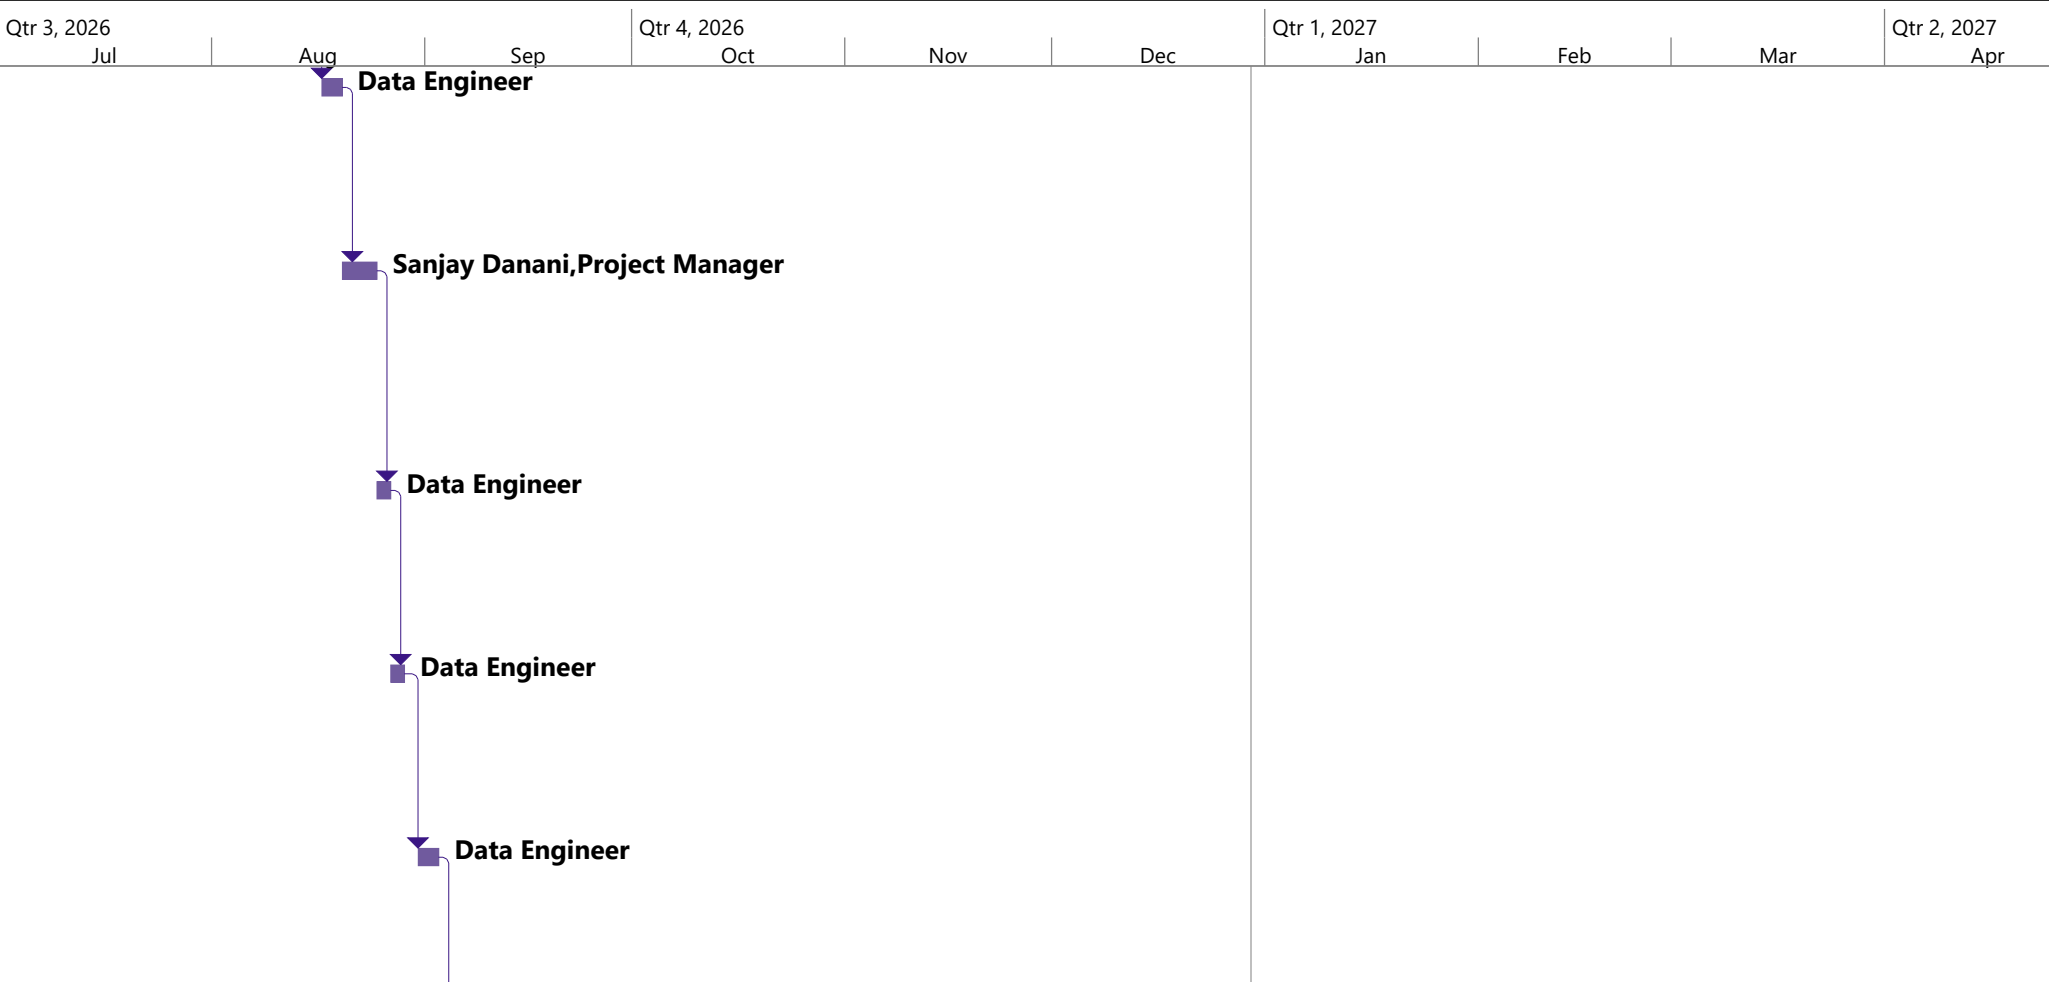


Project: The Cage Data Analytic Date: Sun 14/06/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

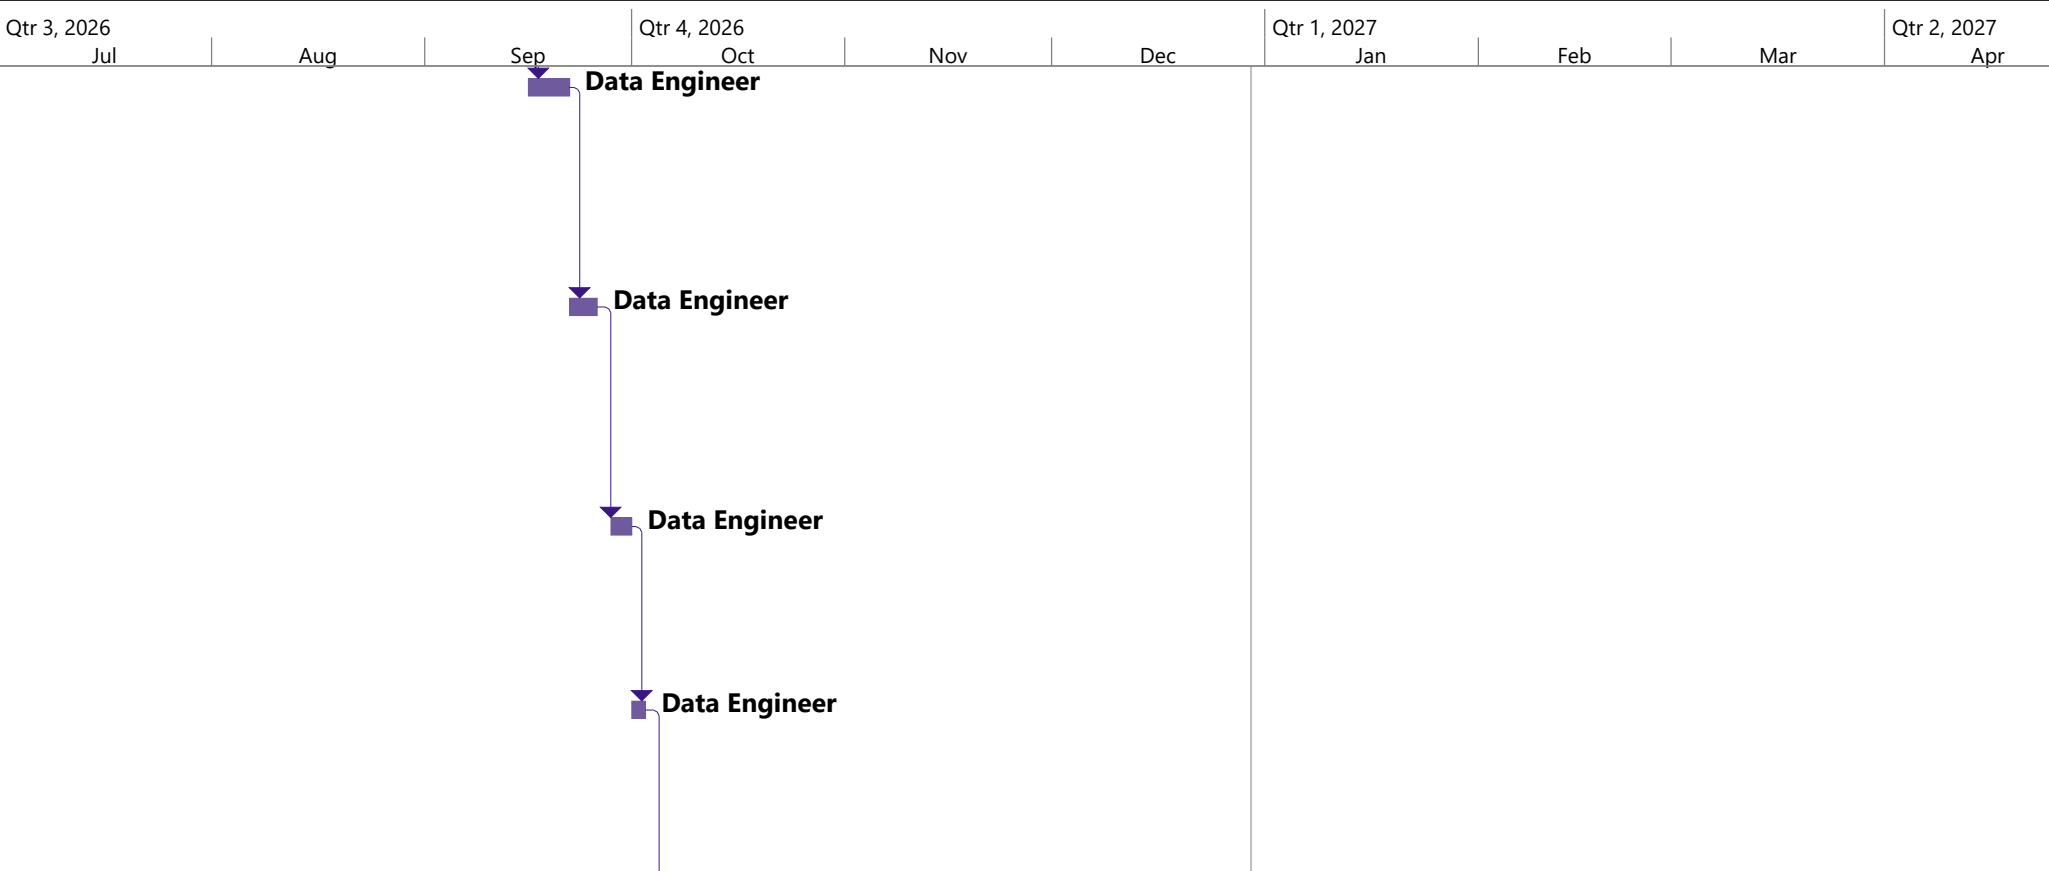


Project: The Cage Data Analytic Date: Sun 14/06/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

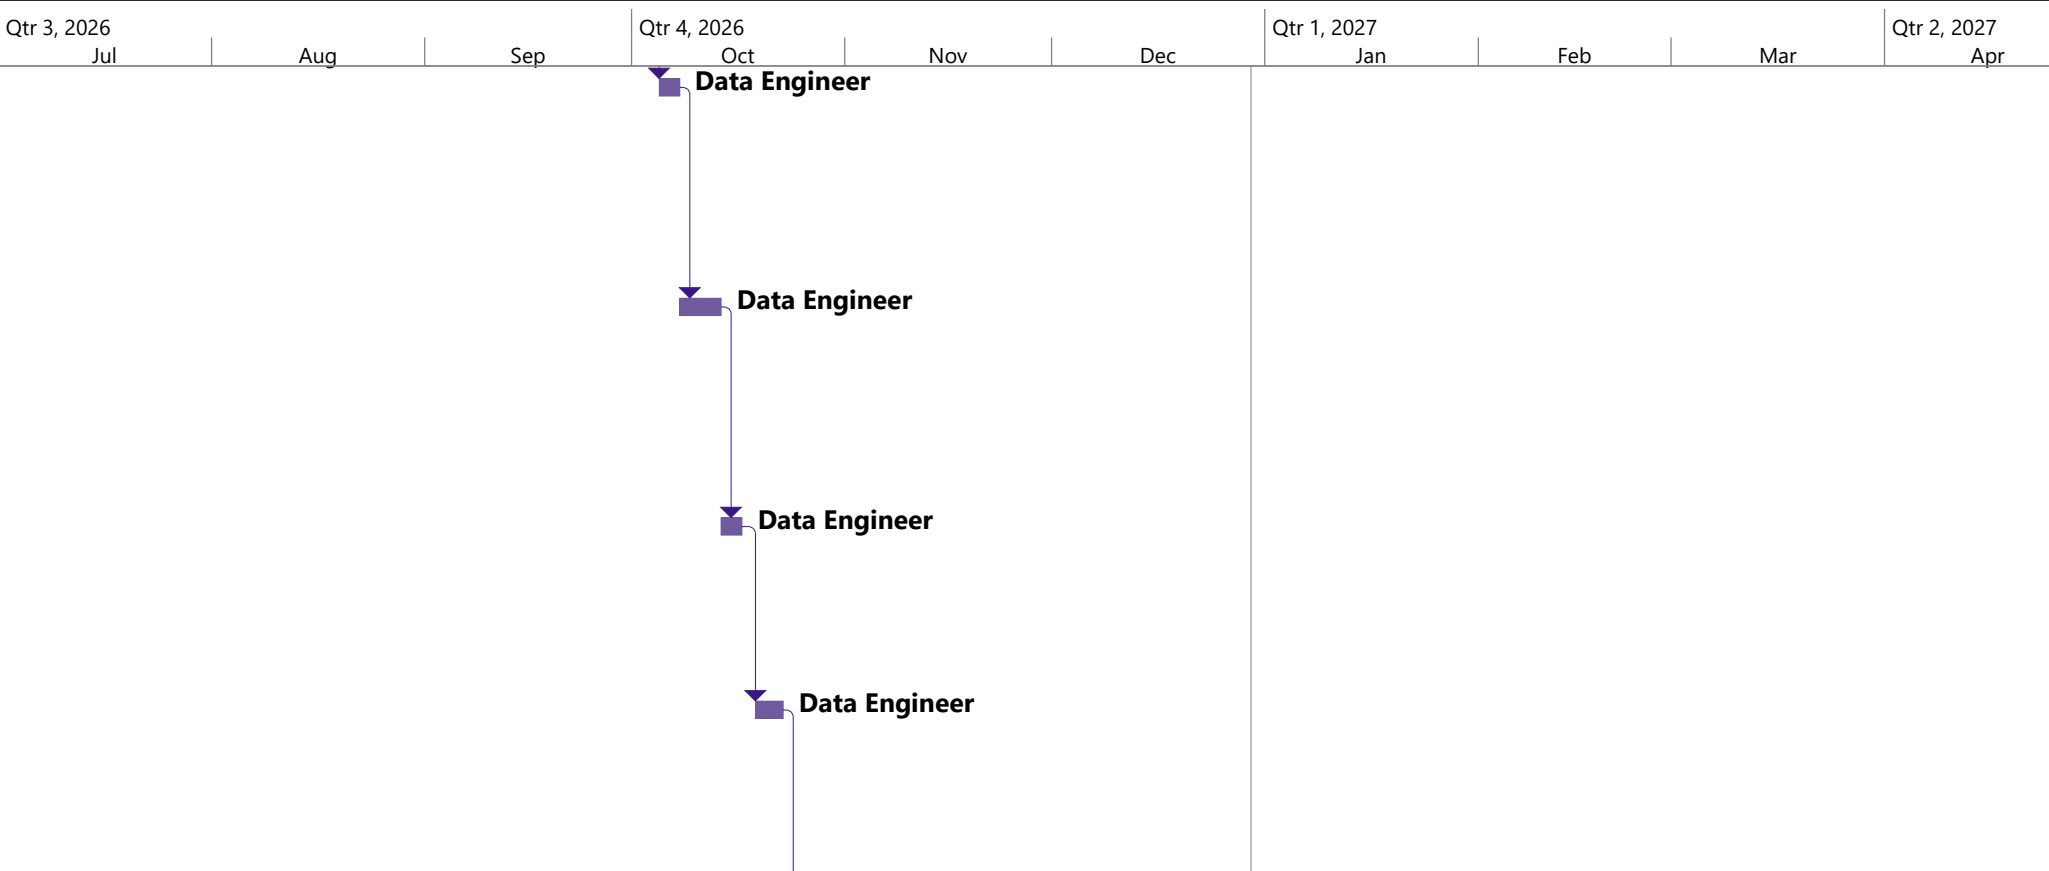


Project: The Cage Data Analytic Date: Sun 14/06/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

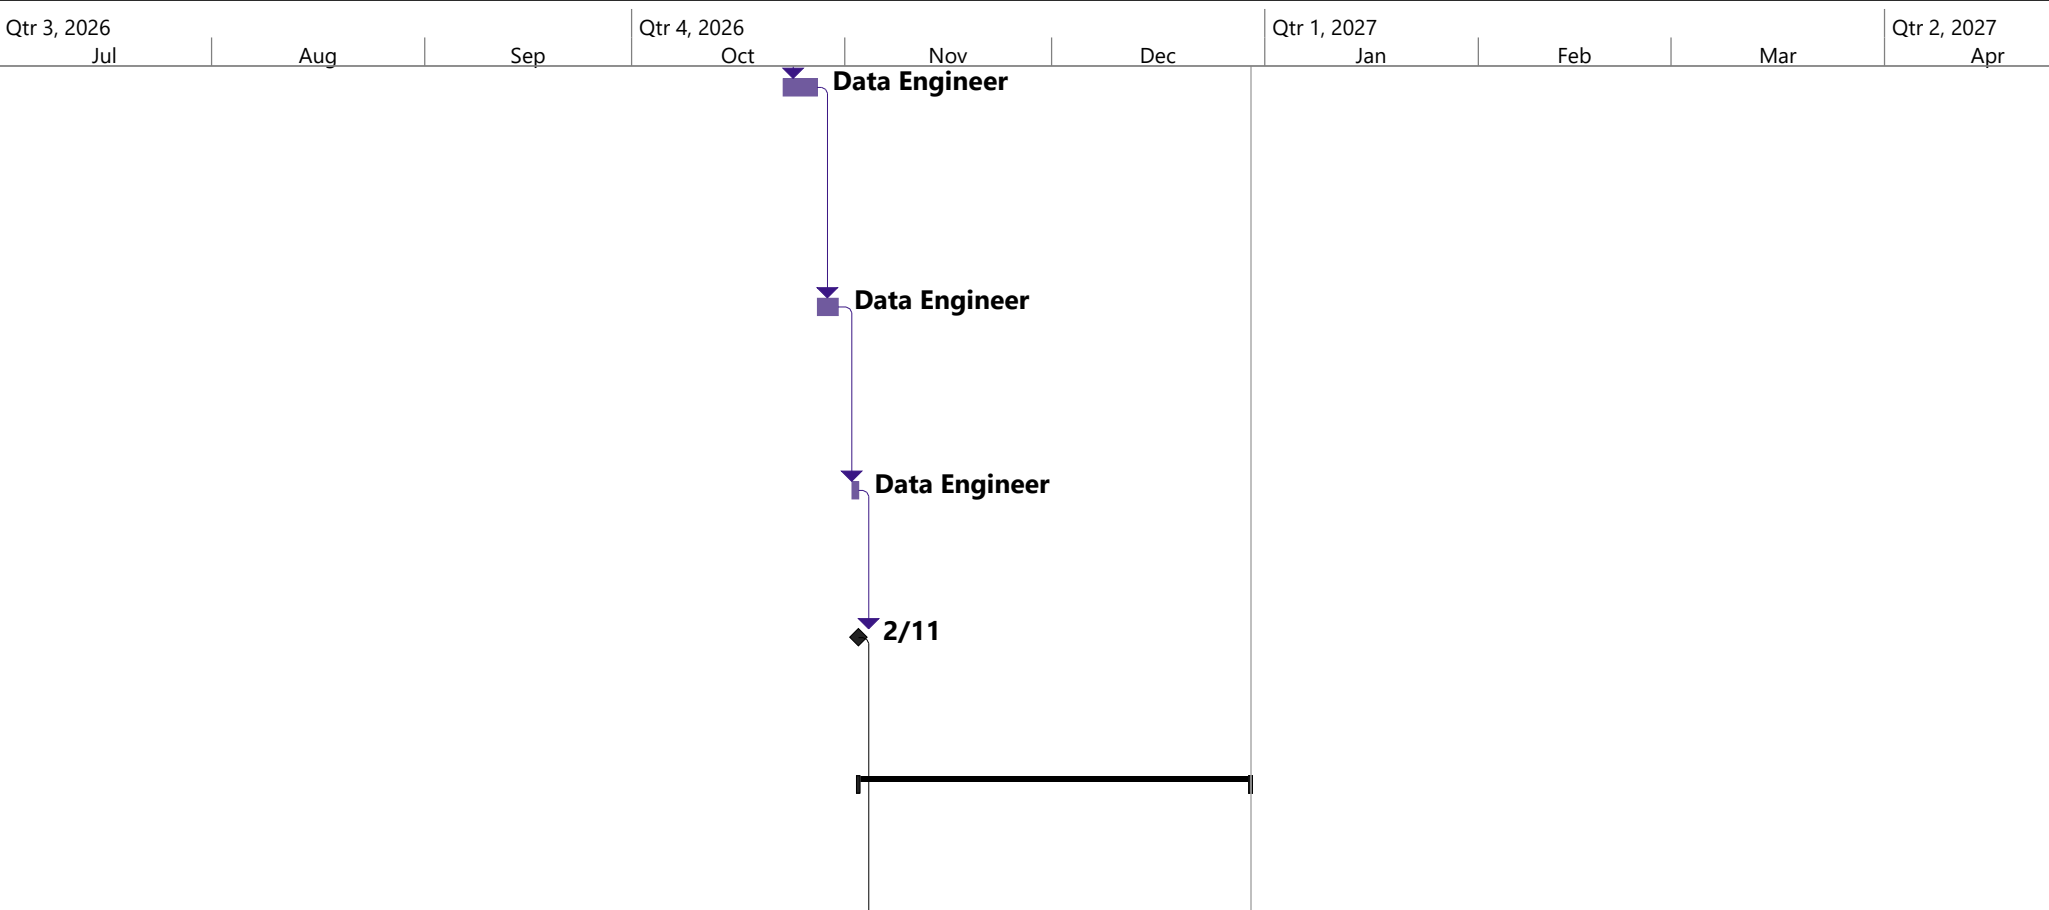


Project: The Cage Data Analytic Date: Sun 14/06/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

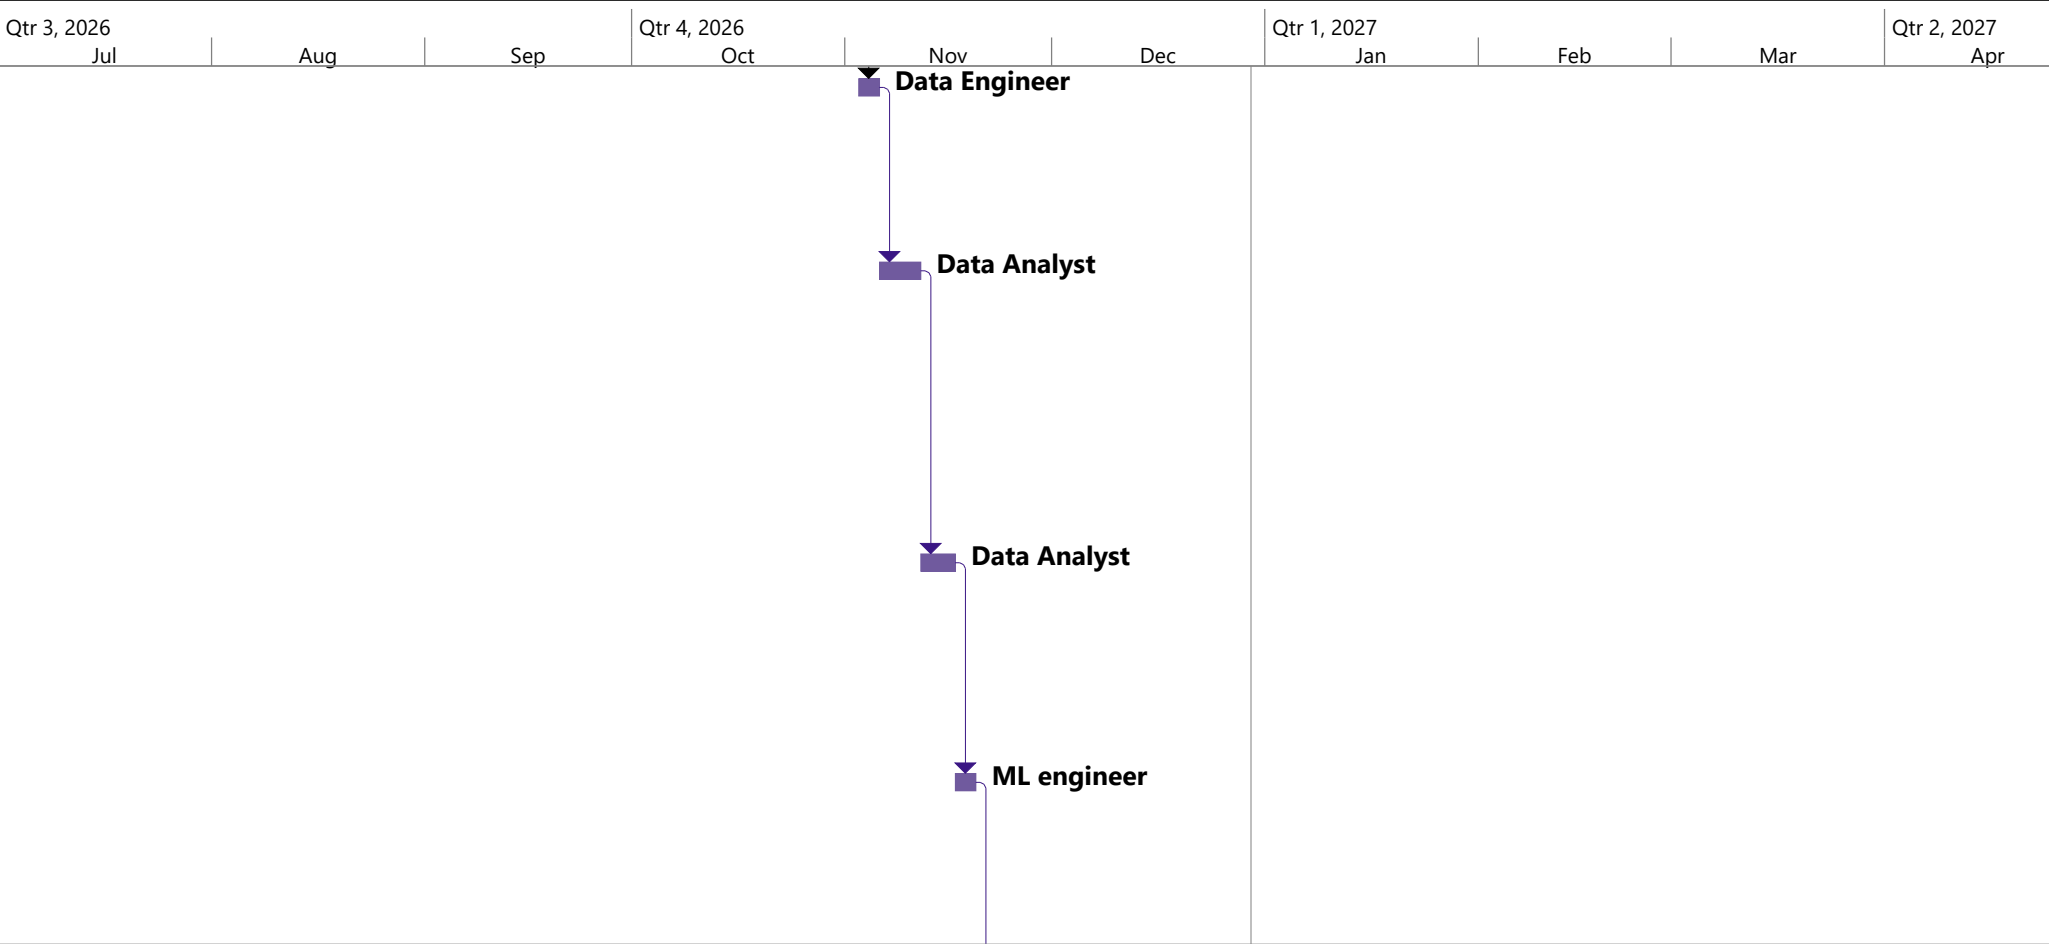


Project: The Cage Data Analytic Date: Sun 14/06/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

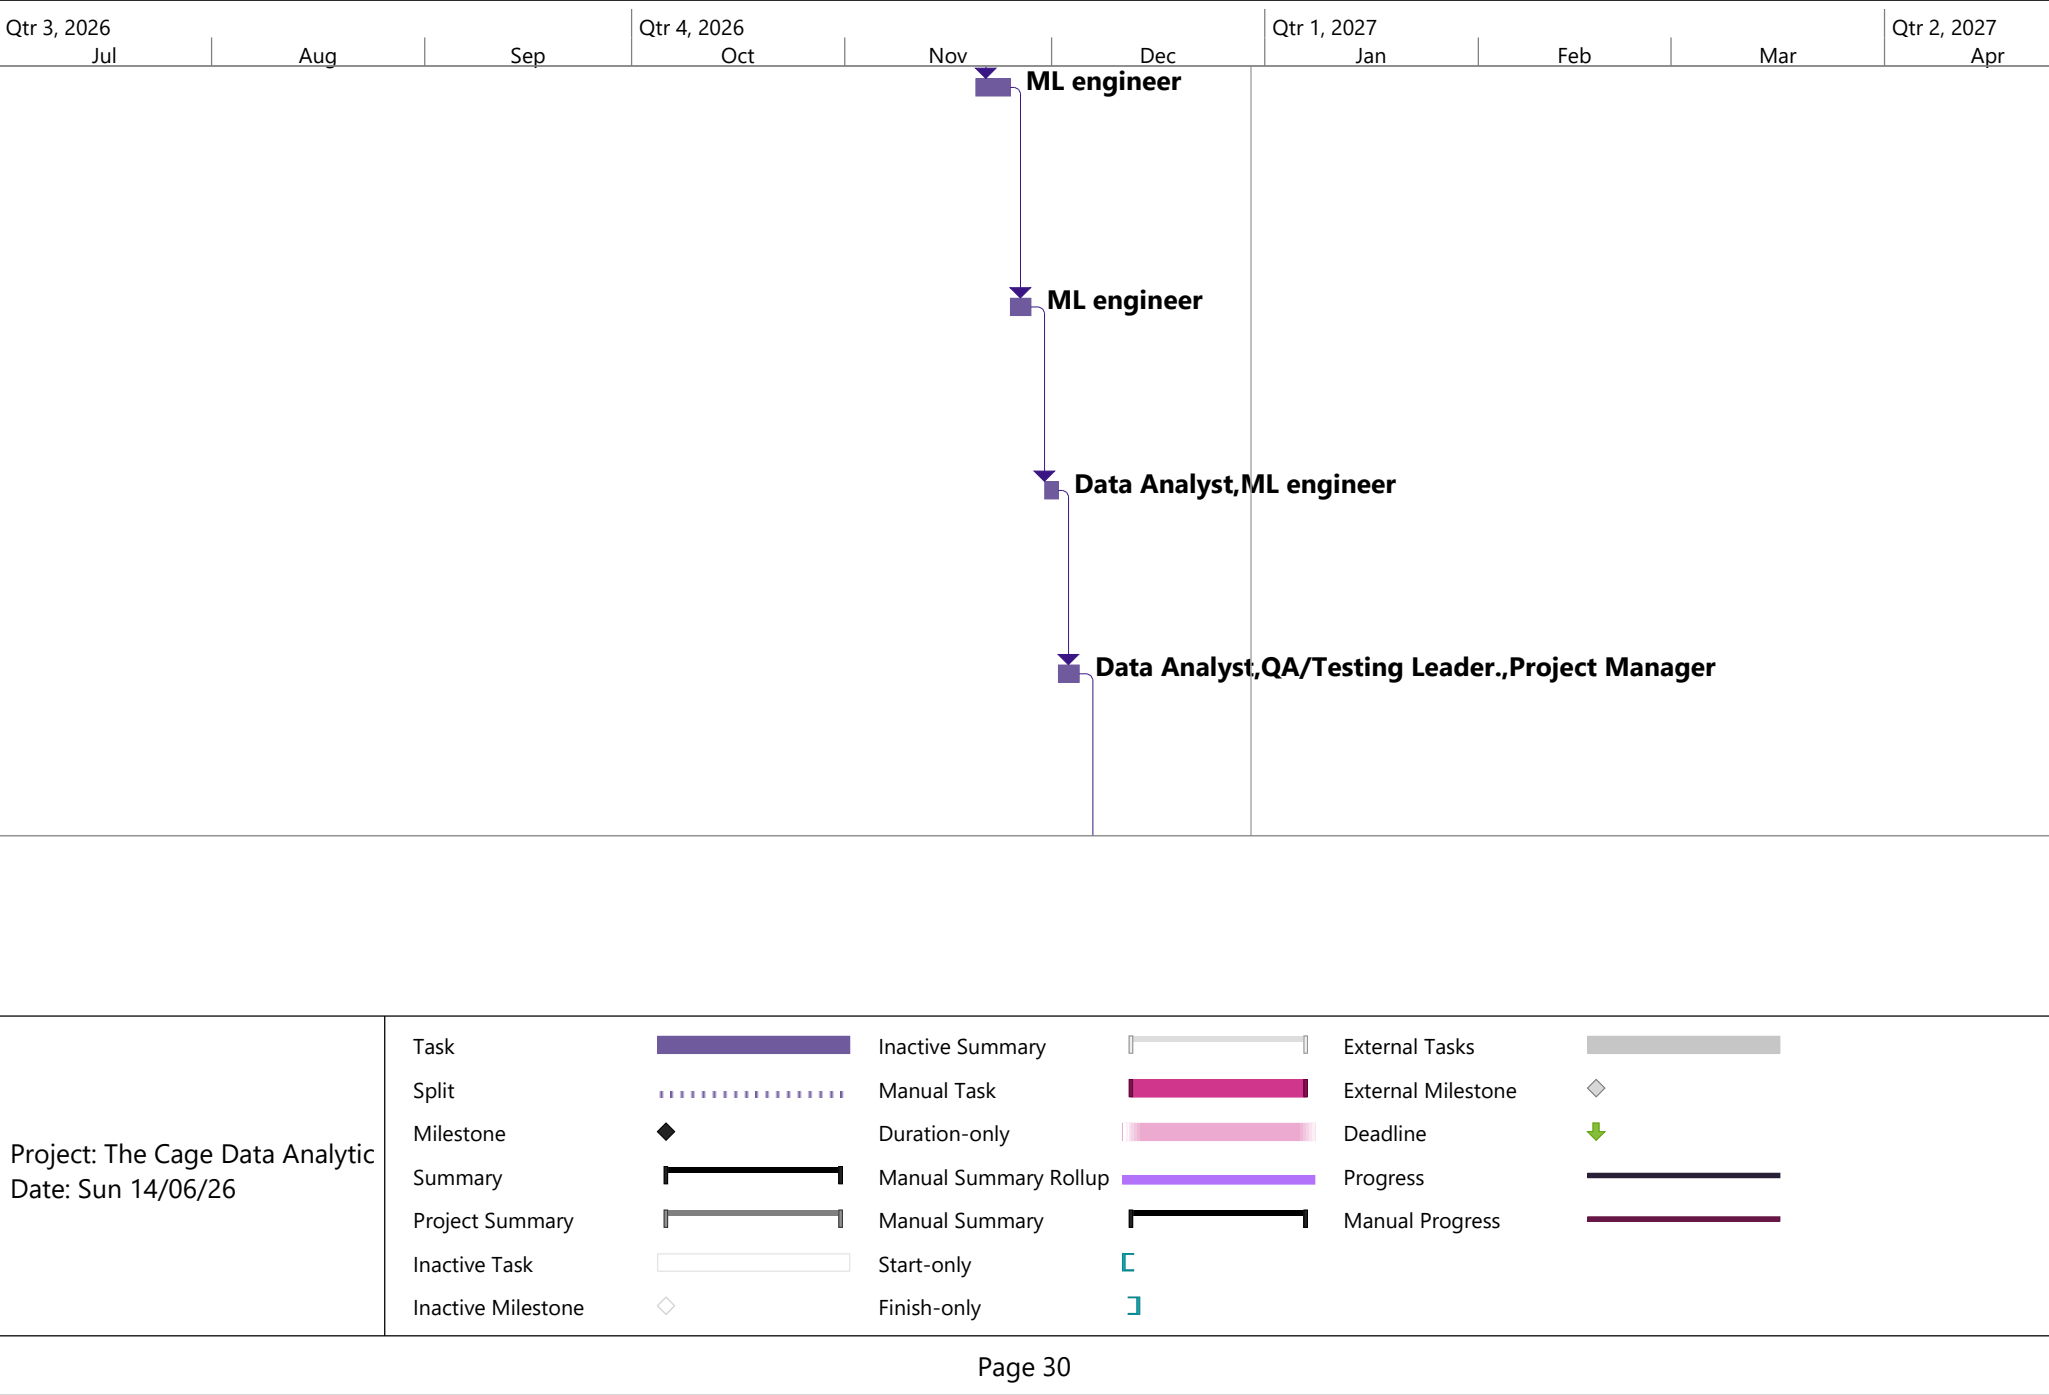

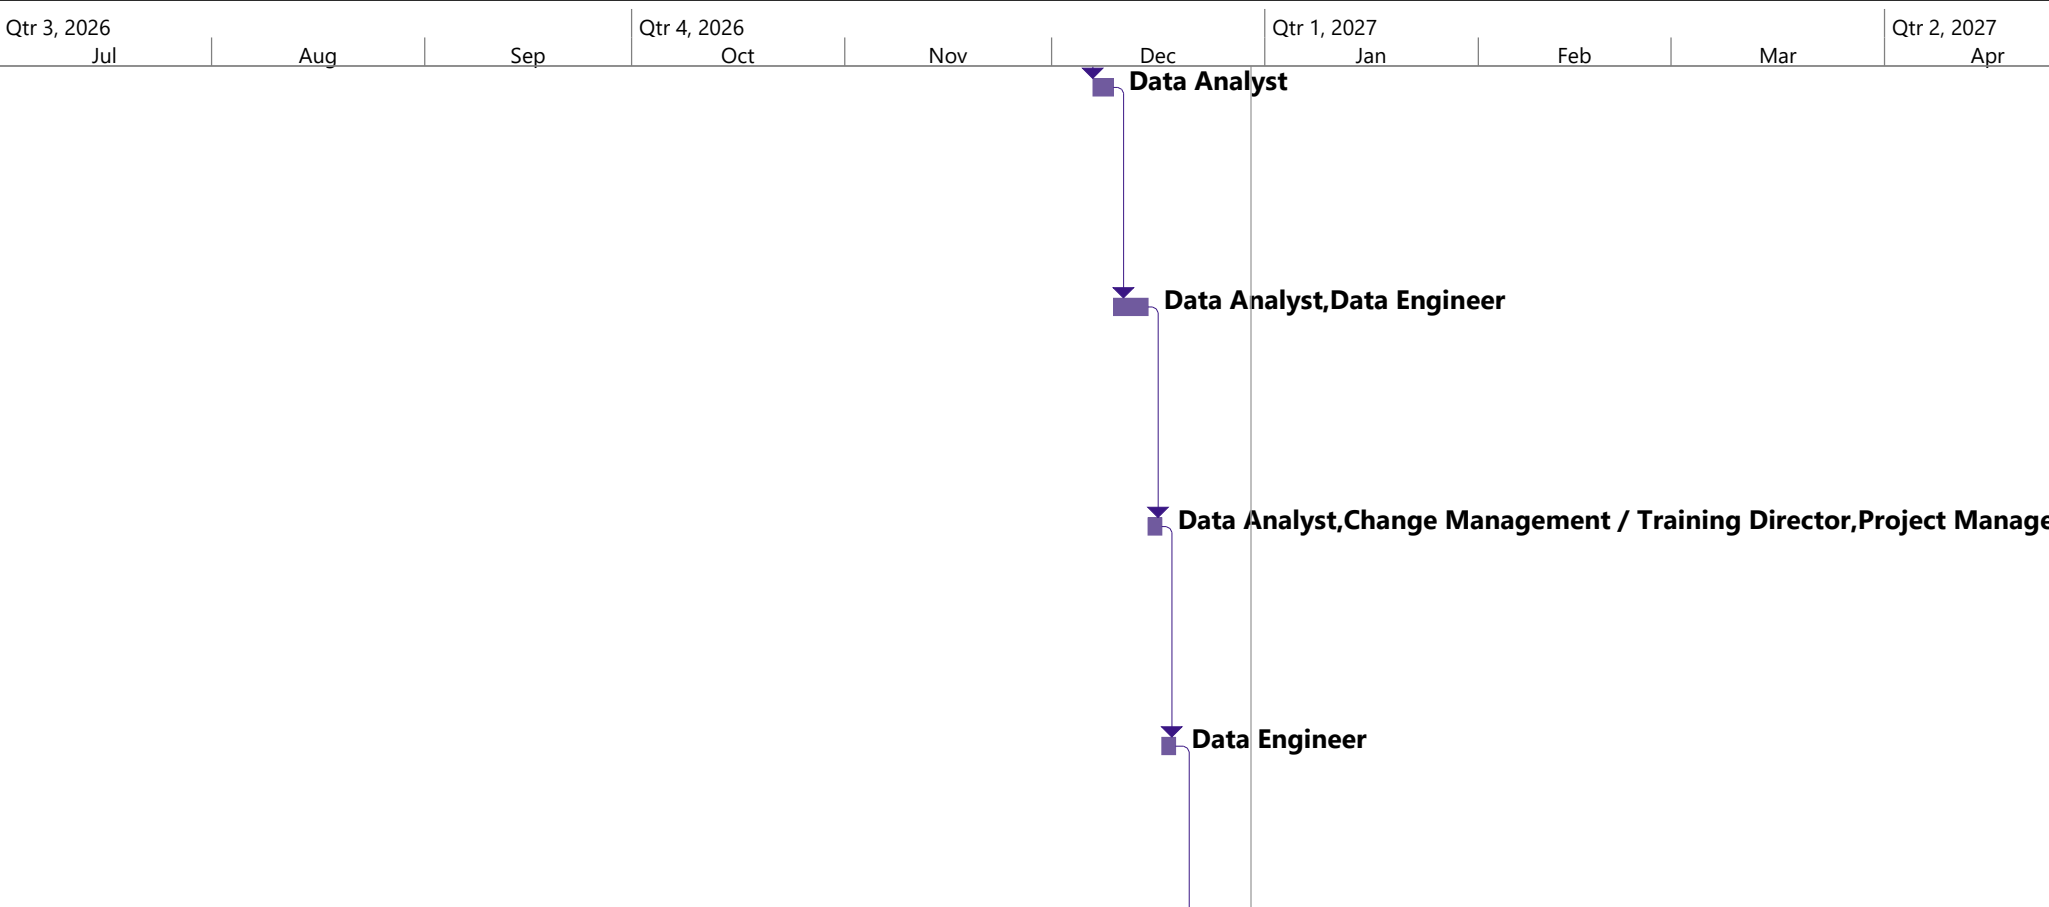

Project: The Cage Data Analytic Date: Sun 14/06/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

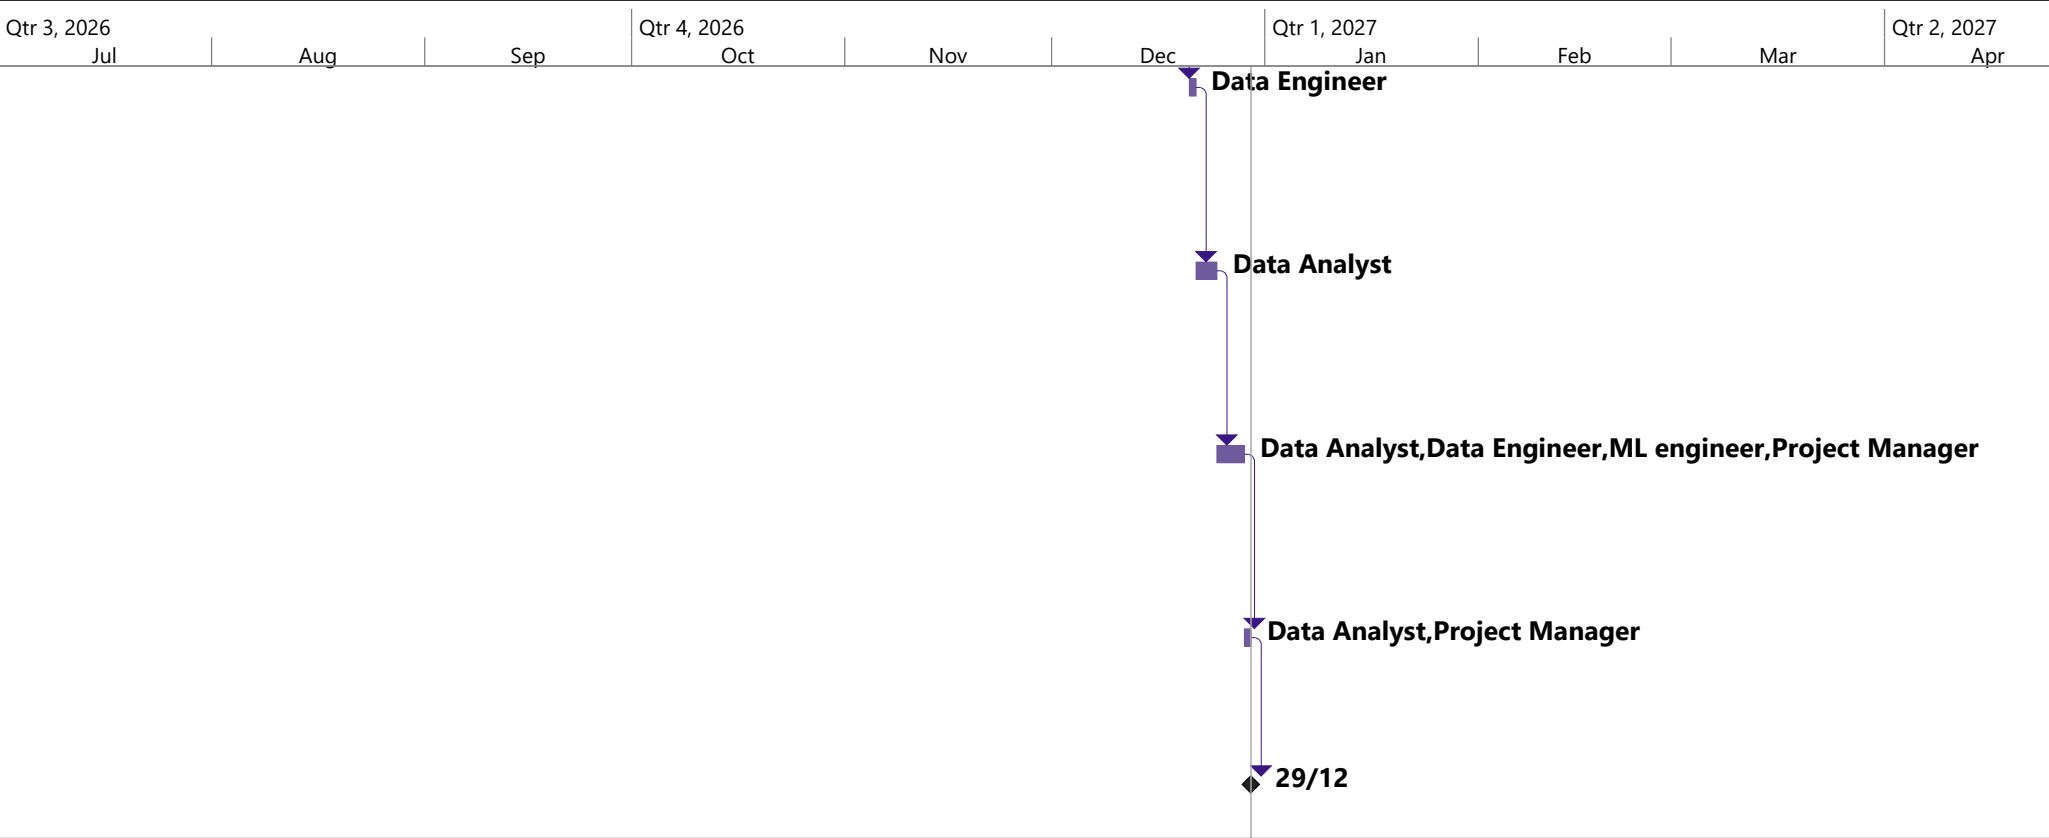

Project: The Cage Data Analytic Date: Sun 14/06/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			
